



Lehenaghmore R I S: Upcoming Works on Togher Road


Update 29th May 2026.

Togher Road:

As mentioned in the most previous update issued on 25th May, the next element of works to be carried out will be the re-construction and vertical/horizontal realignment of the existing Togher Road, involving milling, excavation and resurfacing, from outside Route 14 Bar up to Barrett’s Cross. These works will be done using a combination of temporary traffic management comprising single lane traffic, controlled by vehicle actuated traffic lights, and nighttime road closures as required.

Nighttime Road Closures:

The nighttime road closures, which are required to facilitate the laying of underground ESB ducting, have been postponed and are now scheduled to take place from Wed. 10th June until Friday 12th June 2026 (3 nights) between Barrett’s Cross and Chestnut Drive on the Togher Road, and will be in effect between 19.00 each night until 6.00 the following morning. Local access will be provided for, and diversion routes will be signposted. Location of closure shown in red in the map below:

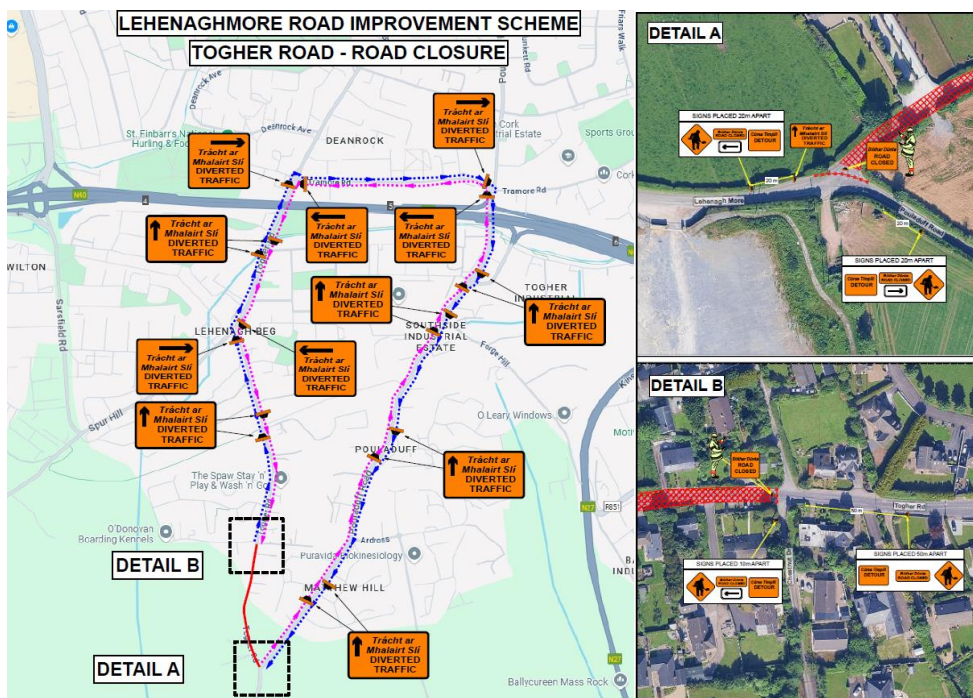



Comhairle Cathrach Chorcaí
Cork City Council



Road Surfacing Works:

The road surfacing works which include milling, excavation and surfacing will commence on the Togher Road on Tuesday 2nd May.

These works will be progress for the whole of the week including Saturday 6th June with early starts as 6.00 am planned on Thursday 4th June and Friday 5th June.

During week commencing 8th June, works will be taking place uphill from the end of the footpath on the right-hand side.

For a 3-week period commencing 15th June kerb laying and footpath works will be taking place uphill from the footpath on the left-hand side.

A further week of surfacing works is scheduled commencing Monday 22nd June 2026 to completed the surfacing from Route 14 Bar to Barrett's Cross.

All of the above works will be completed under temporary traffic management comprising single lane traffic.

We would like to apologise for the inconvenience caused by these works and to assure you that they will be progressed as quickly as possible.

Peter O'Donoghue Liaison Officer GLAS Civil Engineering

Lehenaghmore Road Improvement Scheme

086-1911162 podonoghue@glascel.ie

While every effort will be made to adhere to the outlined schedule, unforeseen circumstances such as adverse weather, supply chain disruptions, or other unexpected events may necessitate adjustments. We will endeavor to communicate any significant changes to residents and stakeholders in a timely manner. We will try to minimise the disruption caused during these essential works and apologise in advance for any inconvenience that may be caused.

Glas Civil Engineering Ltd.

